

KEYSTONE
ENGINEERING &
CONSULTING, INC.

166 Center Street Suite #210
Cape Canaveral, FL 32920
Phone: 321-454-7300
Fax: 321-459-2888

Progress Inspection Report #4 **Permit # 18BC03039**

Project Name: East Horizon
Project Address: 401 Highway A1A, Satellite

Progress Report thru 4-13-18
Inspection Visits: 4-11, 4-12-18

Prime Contractor: Chematics
Superintendent: Tim Lystlund

Activities in-progress: 401 building walkway excavations; north elevation shearwall minor spot and loose stucco repairs

INSPECTORS REPORT

Keystone Engineering visited the site on 4-11 and 4-12-18 and also had several conversations with the construction team by telephone throughout the week.

On the 401 building walkways, excavations have been completed on the 3rd, 4th and 5th floor walkways and were in-progress on the 1st and 2nd floors Thursday and Friday. Walkway excavations will be square cut and detailed early next week with a pre-pour inspection scheduled for next Tuesday.

Minor spot repairs and loose stucco repairs were completed on the north elevation shearwall in order to move the swing stage to the east elevation balconies and begin marking out repair areas, scheduled to begin next week.

James E. Emory, P.E.



View of surface excavation in-progress between Units 122/123 on the walkway



View of slab edge excavation in-progress outside Unit 113 on the walkway



View surface excavation in-progress outside Unit 131 on the walkway




View of excavation in-progress between Units 132/133 on the walkway




View of excavation in-progress outside Unit 122 on the walkway showing additional spalled areas marked for excavation



Close up view showing corroded reinforcing steel and additional spalling marked for repair on the walkway outside Unit 122

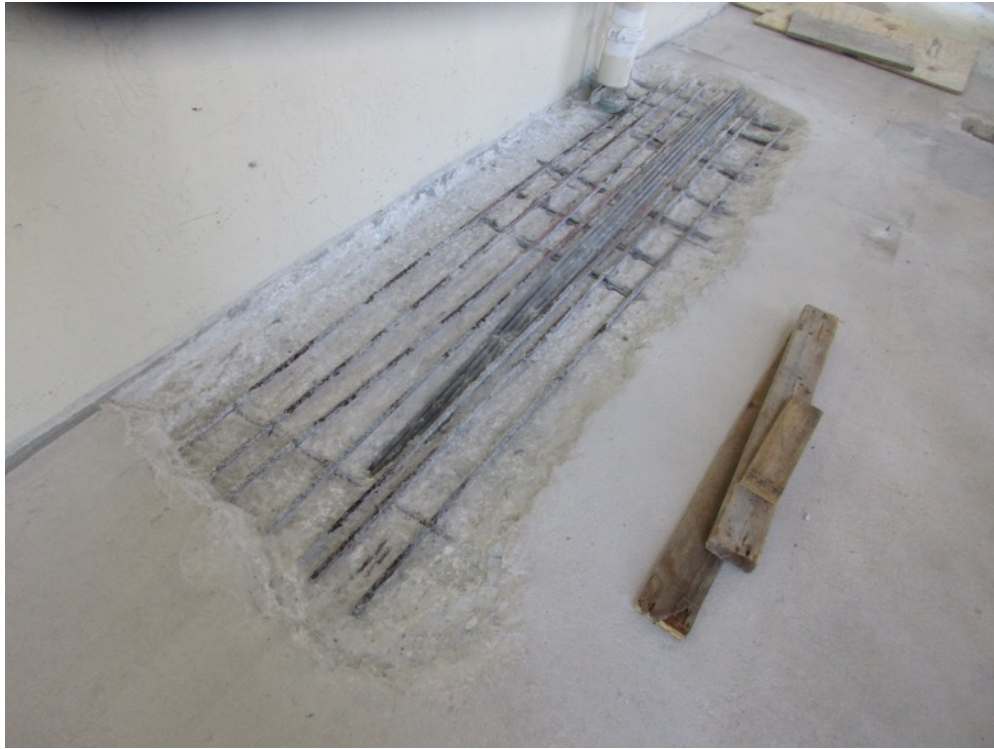

View of excavation in-progress between Units 122/123 on the walkway

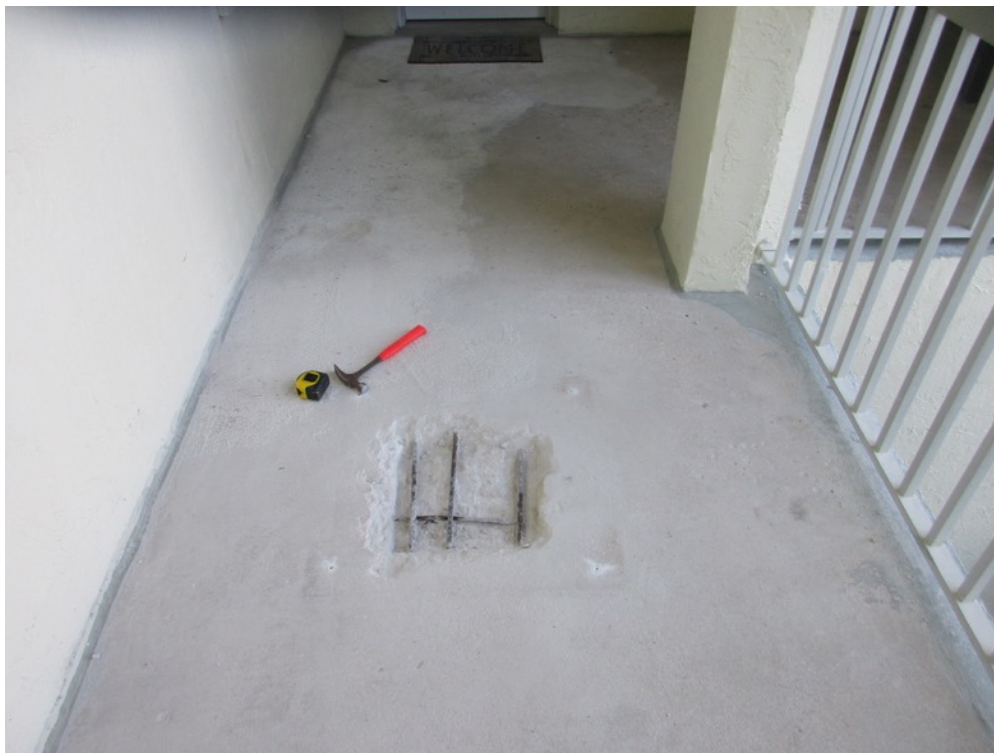

View of surface excavation in-progress outside Unit 113 on the walkway



View of minor spot repairs completed on the north elevation shearwall
